

Jira Scrum Practical / Lab

SE Lab 2

Name: Gagandeep N

SRN: PES1UG24AM367


1. Objective



To create and manage a Scrum project in Jira for a healthcare consent-management system, covering project setup, Epic and Story creation, sprint planning, sprint execution through the Jira board, and analysis of Jira reports such as the Sprint Burndown Chart.

2. Epics

Three Epics were created to group the related user stories by functional area:

- SCRUM-1 — Consent Management
- SCRUM-2 — Diagnostic Record Access
- SCRUM-3 — Consent Monitoring & History

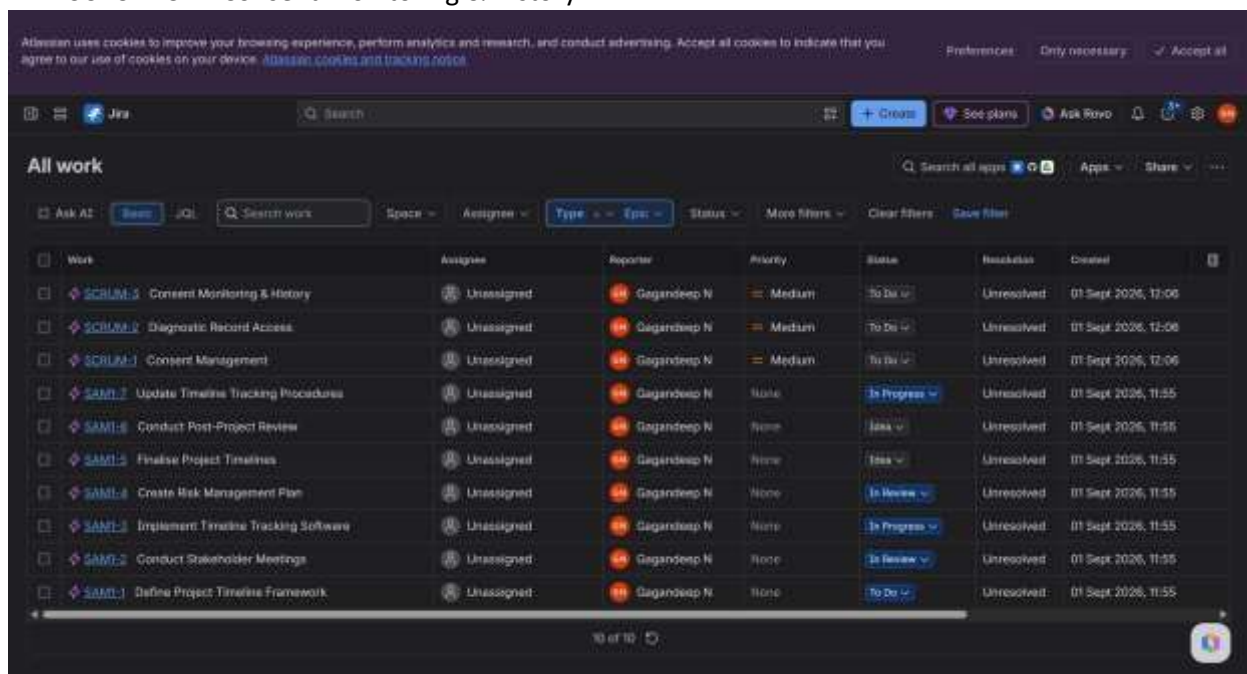

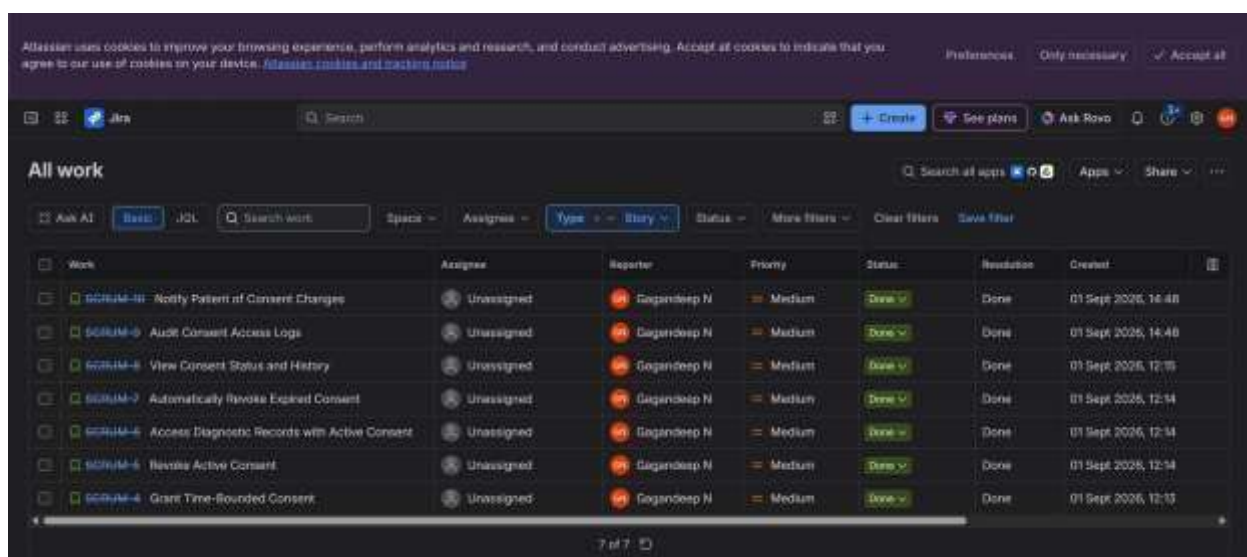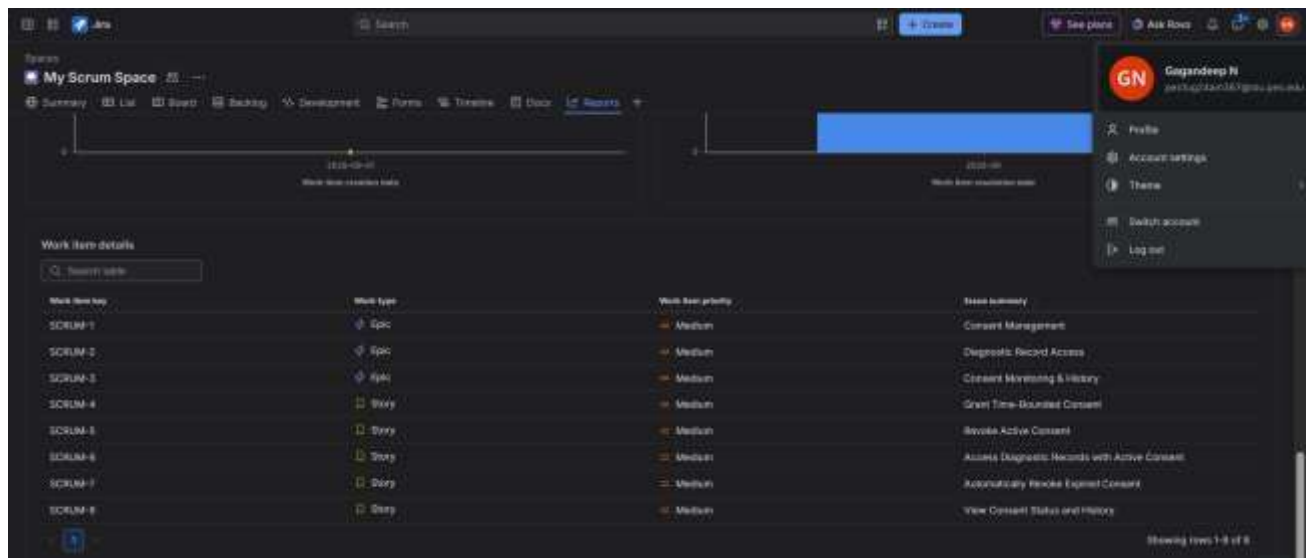

3. Sprint Planning

Sprint 1




Sprint 1 was created and the five stories SCRUM-4 to SCRUM-8 were added to it from the backlog. Sprint 1 was then started, running from 1 September 2026 to 8 September 2026.

Sprint 2

Sprint 2 was created and the remaining two stories, SCRUM-9 (Audit Consent Access Logs) and SCRUM-10 (Notify Patient of Consent Changes), were added to it.

4. Sprint Execution / Simulation

Each story was moved across the Jira board through the standard workflow statuses: To Do → In Progress → In Review → Done. The progression below is shown for Sprint 2 (SCRUM-9 and SCRUM-10); the same workflow was used to move SCRUM-4 to SCRUM-8 to Done during Sprint 1, as confirmed in Figure 4.

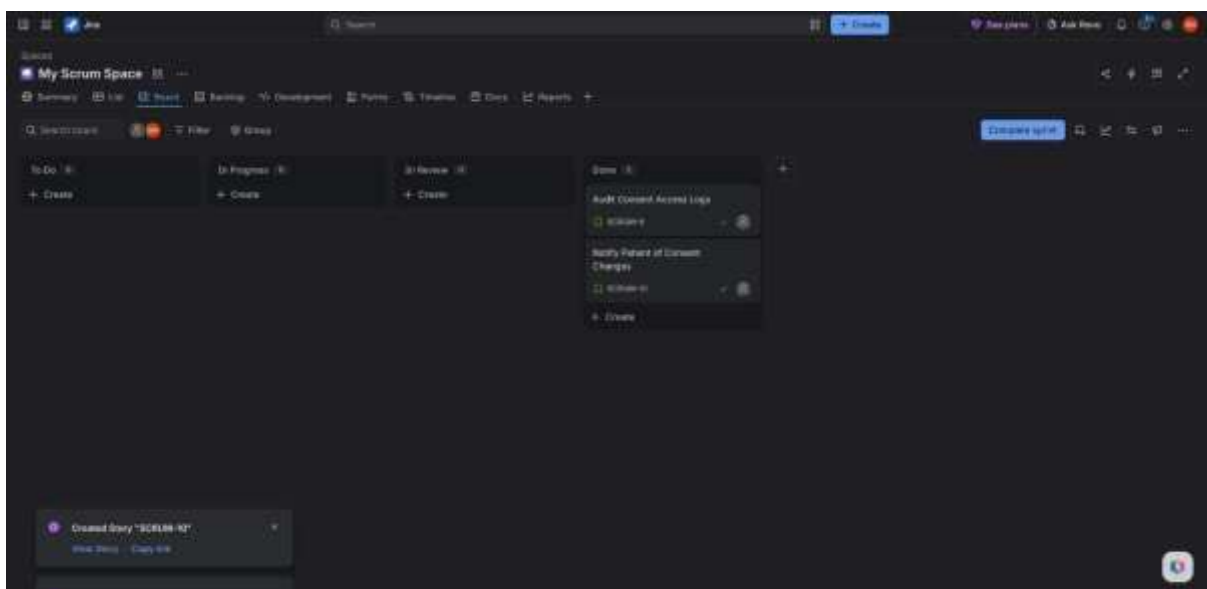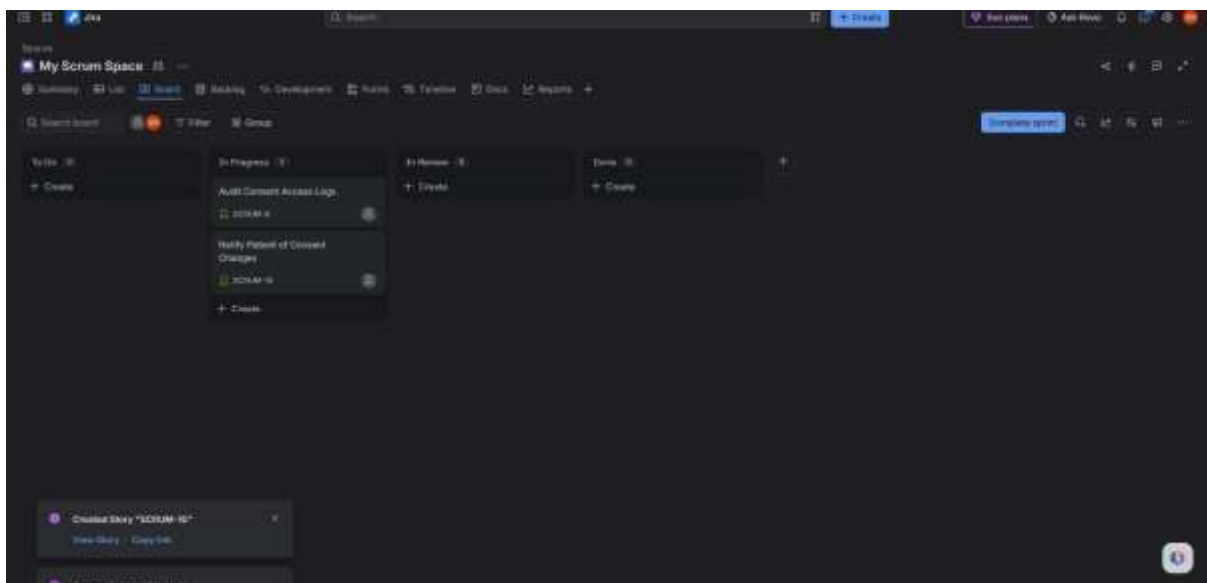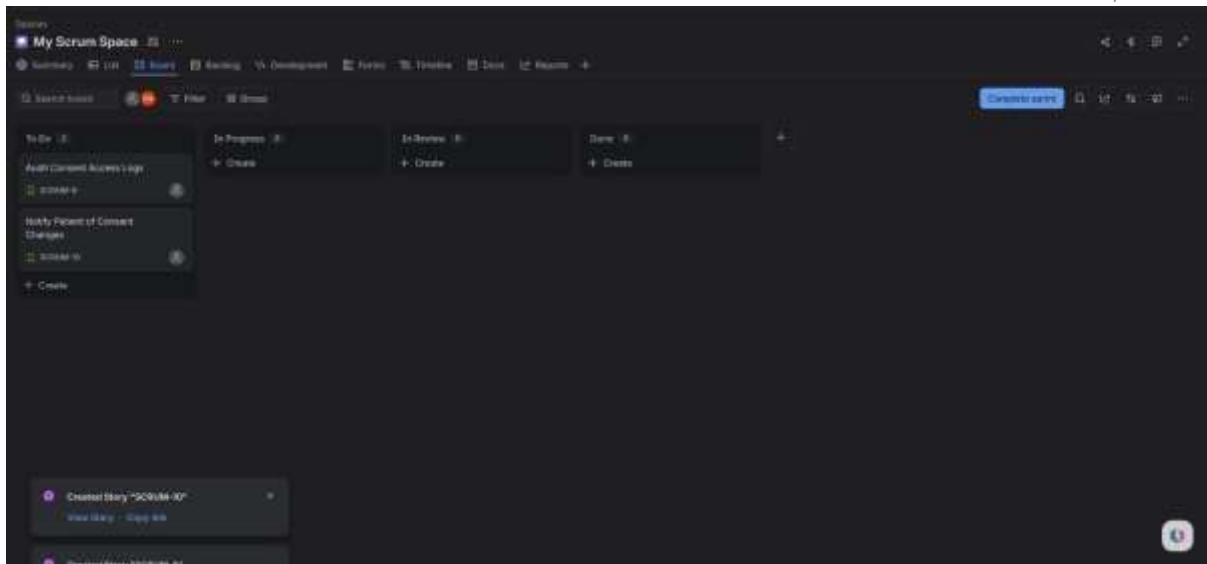


5. Jira Reports

The Reports section of the project was used to review overall progress:

Sprint Burndown Chart

The Sprint Burndown Chart for Sprint 1 shows the ideal burn-down guideline against the remaining story points, indicating how the team's remaining work was expected to reduce over the sprint duration (1–8 September 2026, 18 story points at sprint start).

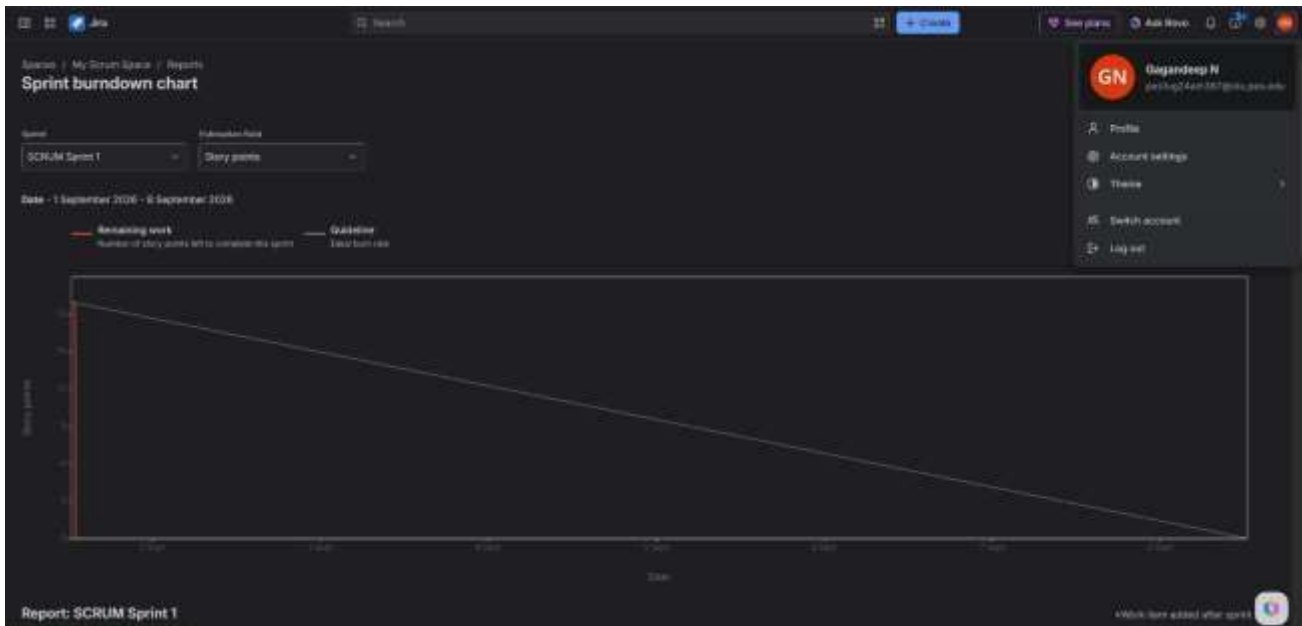

Project Reports Dashboard

The Reports dashboard summarises the project: 8 work items in total, split between Done and To Do status and between Story and Epic type, along with the work item creation trend and cycle time.



Reflection Questions and Answers

1. Did your estimations reflect the actual effort?

Answer:

Yes, the story point estimations provided a reasonable representation of the effort required for the user stories. The stories were assigned different points based on their complexity and expected implementation effort. During the simulated sprint, the work items were successfully completed, indicating that the estimates were generally appropriate. However, in a real project, the estimates could be refined further using actual development data and team feedback.

2. Was your backlog well-prioritized?**Answer:**

Yes, the backlog was organized according to the importance and functionality of the requirements. The major functional areas were first represented as Epics, and the related User Stories were organized under them. Story points were assigned to indicate the relative effort required for each story. This made it easier to select suitable work items for the sprints and manage the overall workload.

3. How did your simulated sprint align with your plan?**Answer:**

The simulated sprint followed the planned Agile workflow by moving the selected User Stories through the different stages of the Scrum board. The stories progressed from **To Do → In Progress → Done**, representing the completion of the planned work. Sprint 1 was successfully completed, and a second sprint was also created and populated with additional work items. Overall, the simulation demonstrated how planned backlog items can be executed and tracked using Scrum.

4. What insights did the burndown chart give about your team's capacity?**Answer:**

The burndown chart showed how the remaining work decreased as the sprint progressed. It provided a visual indication of the team's ability to complete the planned Story Points within the sprint period. Since the planned work was completed, the chart indicated that the team was able to handle the selected workload successfully. The chart can also be used in future sprints to improve estimation and avoid committing to either too much or too little work.
